



March 1, 2023

Rosemary Chiavetta, Secretary
Pennsylvania Public Utility Commission
Commonwealth Keystone Building
400 North Street, 2nd Floor
Harrisburg, PA 17105-3265

**Re: Docket No. C-2012-2308997
Settlement Compliance Status Report**

Dear Secretary Chiavetta:

The following settlement status report is submitted by UGI Utilities, Inc. – Gas Division (“UGI Gas”) in compliance with the Opinion and Order entered by the Pennsylvania Public Utility Commission (“Commission”) on February 19, 2013 (“Final Order”) in Docket No. C-2012-2308997. Please note as of October 1, 2018, UGI South formerly known as “UGI Gas Division”), UGI Central (formerly known as “UGI Central Penn Gas, Inc.”), and UGI North (formerly known as “UGI Penn Natural Gas, Inc.”) merged into UGI Gas. As required by the Final Order in Docket No. C-2012-2308997, UGI Gas is providing this bi-annual progress update for the accelerated main replacement requirements as contemplated by the Joint Settlement Petition approved by the Commission in the Final Order.

As provided in the Joint Settlement Petition, UGI will retire or replace cast iron mains over a fourteen-year time period commencing with the first full calendar month after the date the Final Order was entered. Attached Figure (1): *Cast Iron Main Plan Inventory vs Actual Inventory* provides a chart showing progress (in terms of actual and planned replacements) towards replacing all cast iron main by the end of February 2027. On average, approximately 29 miles of mains must be replaced or retired each year to reach completion in the stipulated timeframe to adhere to the schedule. As of December 31, 2022, the remaining known cast iron main inventory was reduced to 79 miles, slightly ahead of the originally planned target to have 117 miles remaining by this date.

Attached Figure (2): *Bare Steel / Wrought Iron Plan Inventory vs Actual Inventory*, provides a chart showing progress (in terms of actual and planned replacements) towards completing the replacement of bare steel and wrought iron mains over the 30-year replacement time period which began October 2011. As of December 31, 2021, the remaining known inventory of bare steel / wrought iron mains was reduced to 851 miles, which is ahead of the originally planned target to have 1,058 miles remaining by this date.

Ongoing interim progress updates on pipeline replacements will be provided to the Bureau of Investigation and Enforcement’s Safety Division, until the next status report due in 2025.

Sincerely,



UGI Utilities, Inc.
1 UGI Drive
Denver, PA 17517

/s/ Pamela Jocsak
Pamela Jocsak
VP Engineering
UGI Utilities, Inc.

Figure 1
Cast Iron
Plan Required Vs. Actual Inventory

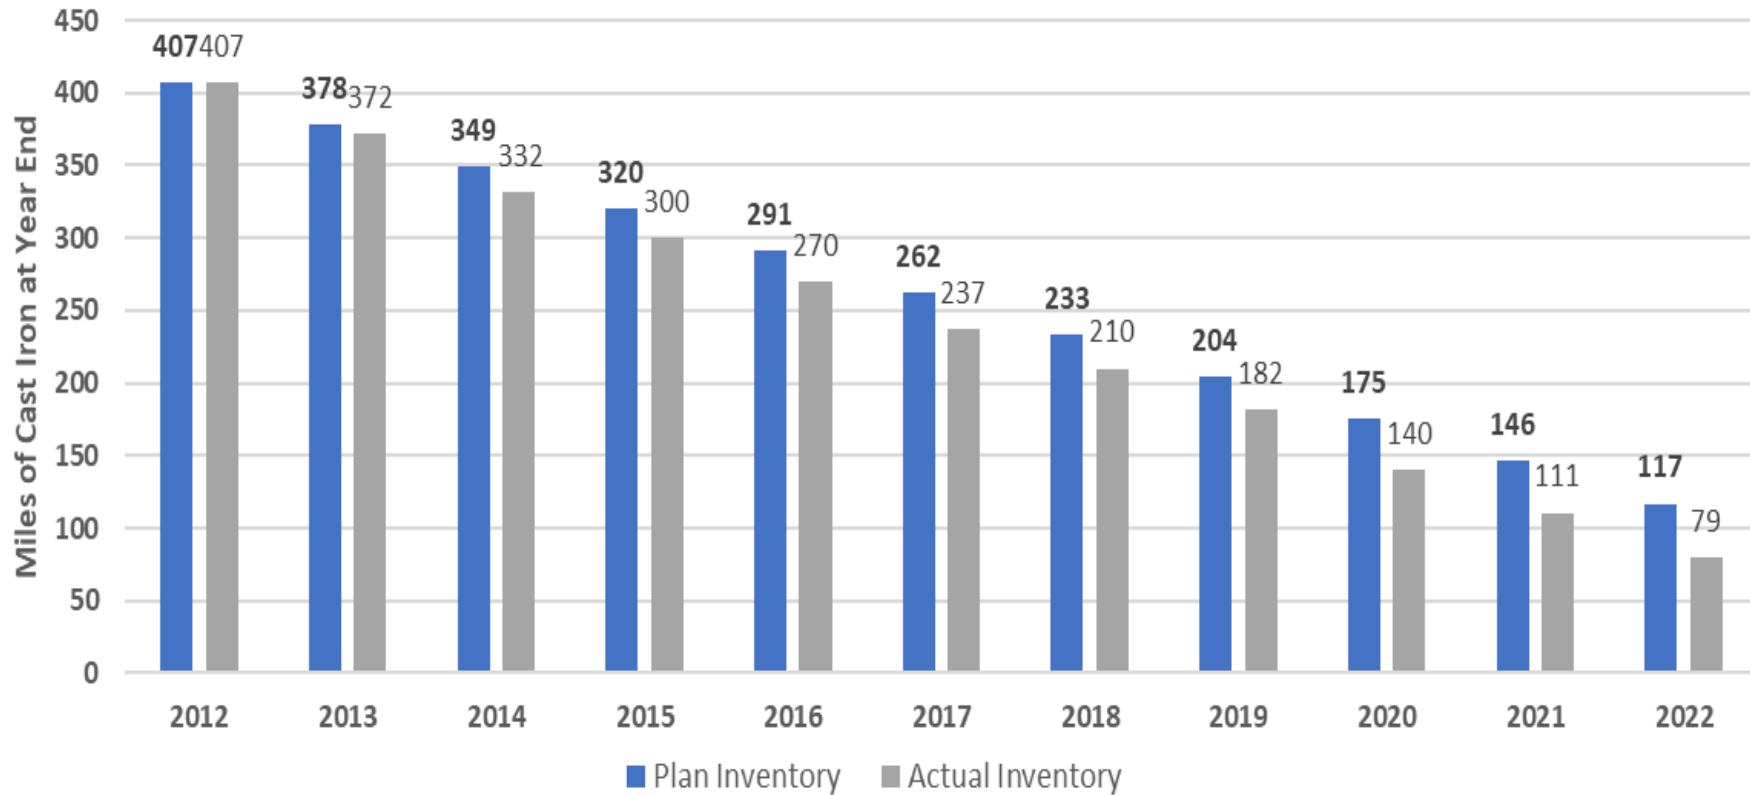


Figure 2
Bare Steel & Wrought Iron
Plan Required Vs. Actual Inventory

